



PHASE 1
Construction of site entrance, internal haul road to working area, and compound.
Install site office, wheel wash and bunded fuel tank.




Phase 2
Removal of vegetation within working area (not between March and August).
Strip topsoils, stockpile as bunding, seed.

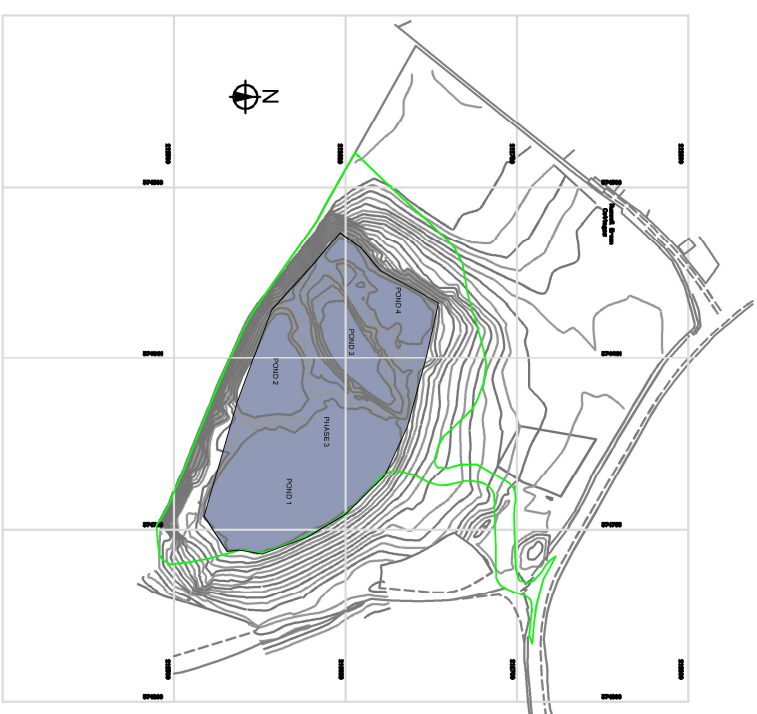

Phase 3
Drain existing ponds.
Clear sludge, level base of ponds.

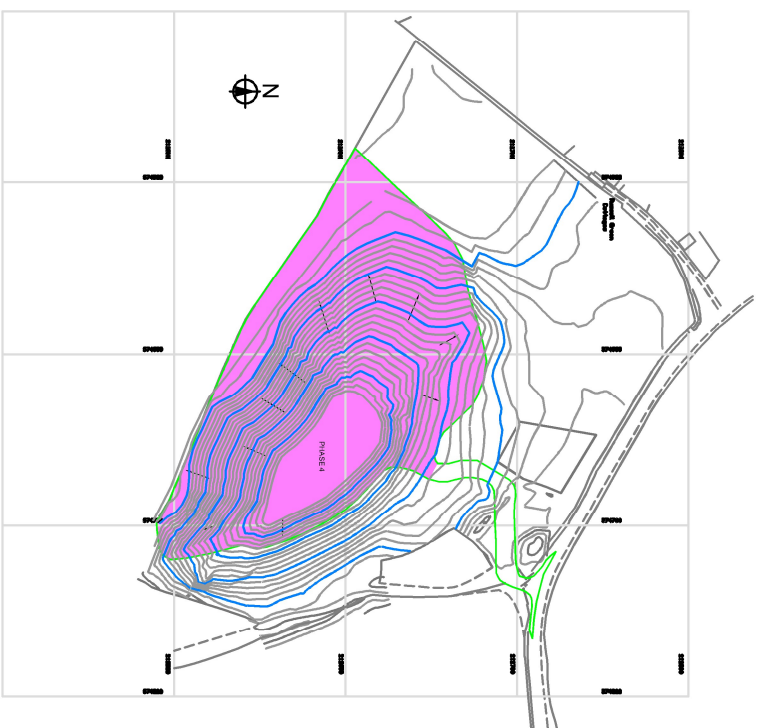

PHASE 4
Stabilise quarry face.
Key-in trenching against slopes, in 250mm horizontal compacted layers from base.
Creation of new pond.

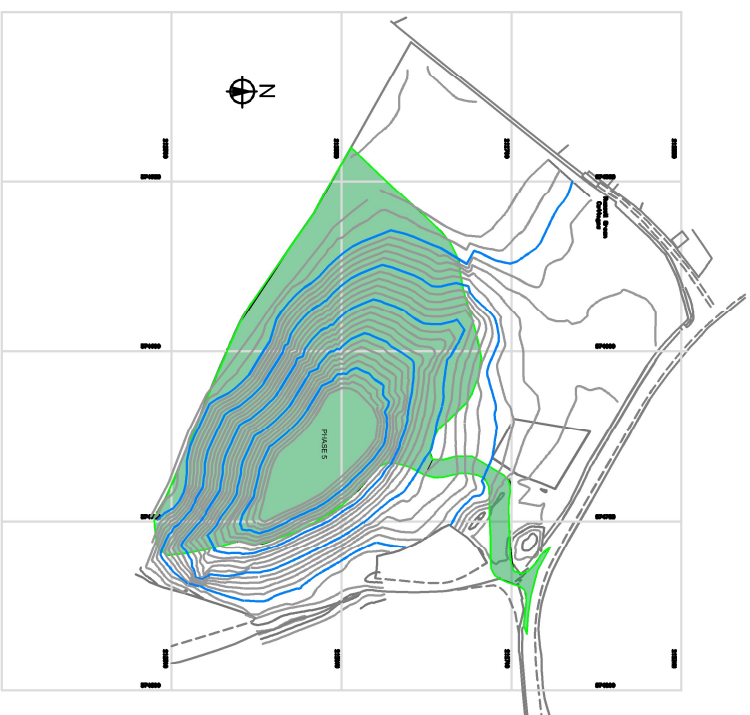

PHASE 5
Whole site landscaping
Removal of Site Infrastructure

Client: Land Logical Dartford Limited

Project: Phasing Plan

INTEGRATED SKILLS LIMITED

EMAIL: info@integrated-skills.com
(www.integrated-skills.com)

Date: March 2024

Scale: NTS

Drn No LLDU/RG/PHS01

REV: A
