[redacted]

AMP8 TDCL Master Plan Full 19 Dec 2025

Maer Lane STW Extract 06 Jan 2026

[redacted]

#	Activity Name	Original Duration	Start	Finish
1	**AMP8 TDCL Master Plan Full 19 Dec 2025**	861d	27-Oct-25 A	12-Apr-29
2	**Work to Win**	861d	27-Oct-25 A	12-Apr-29
3	**15848 - MAER LANE STW_SSO_EXMOUTH**	861d	27-Oct-25 A	12-Apr-29
4	Concept handover to delivery team	0d		27-Oct-25 A
5	High level price by Chandlers w/TD input	20d	28-Oct-25 A	24-Nov-25
6	Budget PE application & AtB	40d	25-Nov-25	22-Jan-26
7	ECC1 Contract award	0d		22-Jan-26
8	ECC1 Contract period - TDCL staff design support	234d	23-Jan-26	06-Jan-27
9	ECC1 Contract period - Site surveys	70d	02-Mar-26*	11-Jun-26
10	EA Disinfection meeting 1 & 2	1d	24-Apr-26*	24-Apr-26
11	Detailed design	120d	09-Nov-26*	12-May-27
12	Land Purchase	124d	11-May-26*	02-Nov-26
13	EA Disinfection meeting 3	1d	25-Sep-26*	25-Sep-26
14	Planning process	180d	15-Jun-26*	08-Mar-27
15	TDCL pricing £10m+	50d	07-Jan-27	17-Mar-27
16	TDCL Internal governance	20d	18-Mar-27	16-Apr-27
17	Price submission, negotiations & acceptance	20d	19-Apr-27	17-May-27
18	Papers uploaded to Diligent (2025 IPC Timetable used)	0d		17-May-27*
19	SWW Governance - Calendar dependent	25d	18-May-27	22-Jun-27
20	EA new STW permit application	61d	29-Apr-27*	26-Jul-27
21	Contract preparation & award	10d	23-Jun-27	06-Jul-27
22	Procurement start	0d	07-Jul-27	
23	Mobilisation	20d	07-Jul-27	03-Aug-27
24	Start on site	0d	04-Aug-27	
25	Civils works	185d	04-Aug-27	02-May-28
26	MEICA	230d	03-Nov-27	04-Oct-28
27	Commissioning	60d	05-Oct-28	04-Jan-29
28	COU	0d		15-Jan-29
29	OA1	0d		12-Apr-29

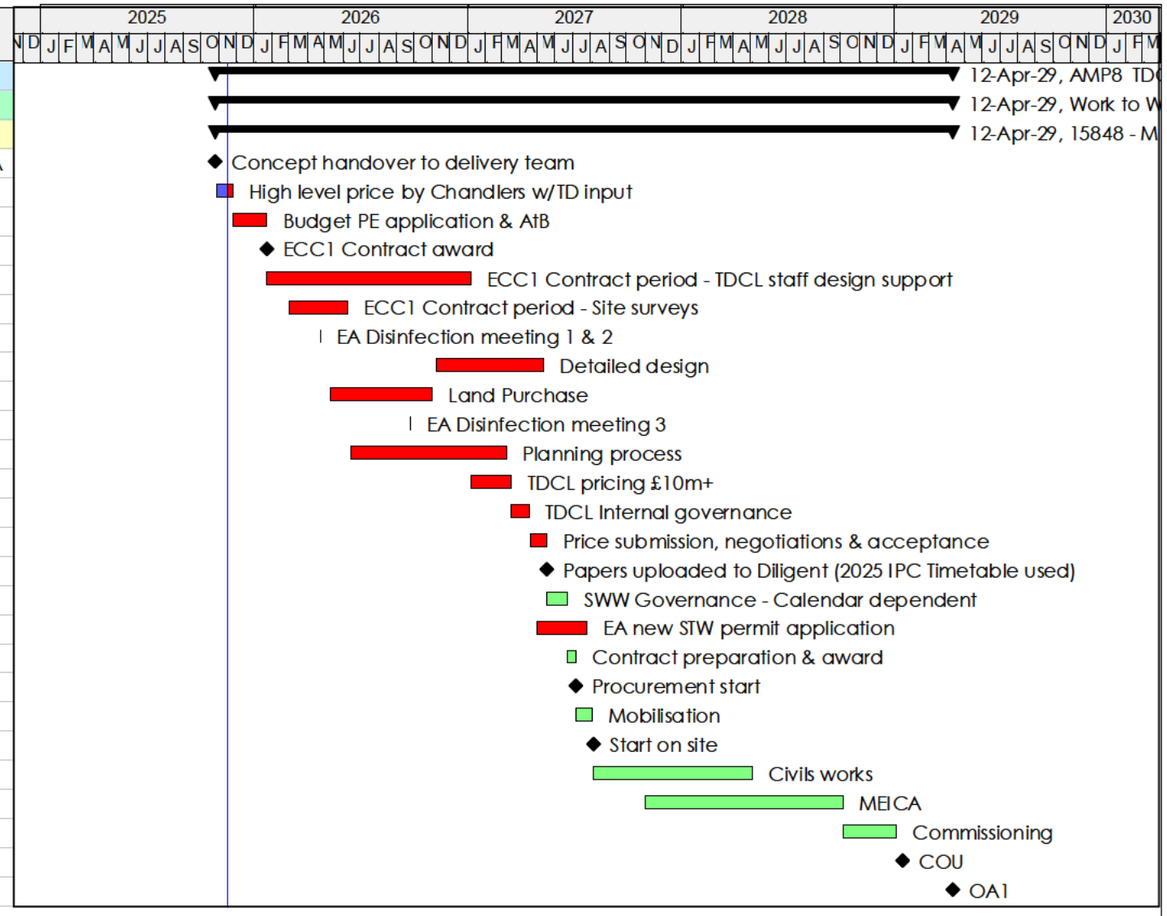

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | Summary

06-Jan-26
